

## Public Works & Engineering

| Item | Work Required                               | Division Responsible | Estimated Start Date | Comments                                     | Status    |
|------|---|----------------------|----------------------|--|-----------|
| 1    | Spread ice in parking area not<br>including | Contracts – Serve    | Week of March 29     |  | Completed |
| 2    | Clear/flush & inspect Culverts              | Contract Services    | Week of March 29     | Work has started                             | Completed |
| 3    | Sign Installations                          | Traffic              | Early April          | Temporary and damaged signs to be reinstated | Completed |
| 4    | Playground Inspection                       | Parks                | Мау                  | To be inspected following park clean up      | Completed |
| 5    | Safety Station Inspection                   | Parks                | May                  | To be inspected following park clean up      | Completed |
| 6    | Bridge                                      | Capital Works        | Early April          | Repair lower rails and cables                | Completed |



| Item | Work Required                                | Division Responsible | Estimated Start Date | Comments   | Status    |
|------|--|----------------------|----------------------|--|-----------|
| 7    | Debris Removal                               | Road Operations      | Mid April            | Drop off Bin and aid with debris removal   | Completed |
| 8    | Debris Removal                               | Forestry             | Mid April            | Remove all Forestry related debris in the park, parking<br>lot and south of the bridge | Completed |
| 9    | Debris Removal                               | Parks                | Mid April            | Remove all debris within the park  | Completed |
| 1 10 | Street Lighting Inspection in Parking<br>Lot | Street Lighting      | End of April         | Completed after ice and Debris is removed  | Completed |
| 11   | Reinstate/adjust Guide Rails – on the        | Contracts – TBD      | End of April         | Completed after Debris removal   | Completed |
| 12   | Tree Planting                                | Forestry             | Mid May              | TBD – if required  | NA        |
|      |  | Parks                |                      |  | Completed |
| 1 14 | Regrading area "dyke" area around<br>area 5  | Parks                |                      | Following completion of Guide Rail works Determine who will completing                 | Completed |





| Item | Work Required   | Division Responsible | Estimated Start Date               | Comments   | Status    |
|------|---|----------------------|------------------------------------|--|-----------|
| 15   | Parking Lot and Driveway – regrading  |                      |                                    | Completed after all restoration works have been<br>completed     | Completed |
| 16   | Repair end post NE corner of Bridge   | Contract Service     | Mid of September following locates | Poste replaced and cables adjusted                               | Completed |
| 17   |   | Contract Service     | October 12-14                      |  | Completed |
| 18   | grade the stone at the parquetted<br>located on N/W corner of Creditview<br>and Churchville | Road Operations      |                                    | Sandalwood Yard staff added addition gravel to remove the divots | Complete  |






| Item | Work Required  | Division Responsible | Estimated Start Date | Comments   | Status    |
|------|--|----------------------|----------------------|--|-----------|
| 19   | Swale improvement to catch basin in<br>front of resident's house | Road Operations      | End of September     | Work will be scheduled in the near future  | Completed |
| 20   | repair signs at Bridge   | Sign shop            | End of September     | Warning Sign at south end of bridge need to be secured.  | Completed |
| 21   | Repair Signs at Creditview                                       | Sign shop            | End of September     | Street name sign for Churchville and Creditview needs to be straighten and secured.              | Completed |
| 22   | Repair Signs at Halstone   | Sign shop            | End of September     | Halstone and Creditview street name sign is on a temp stand and need to be permanently installed | Completed |
| 23   | Clear plant overgrowth along churchville                         | Parks                | End of August        | location is the north side of Church Street between<br>Churchville Road and Victoria Street      | Completed |
|      | Relocate Mailboxes back to firehouse<br>parking lot              | Contract Services    | Mid September        | Mailbox relocated  | Completed |

## Image





| Item | Work Required  | Division Responsible               | Estimated Start Date  | Comments  | Status  | I |
|------|--|------------------------------------|---|---|---|---|
| 25   | New Flap Gate installation at outfall #4<br>near Bridge    | Contract Services                  | End of December 2022  | Replaced with inline check valve in March 2023  | Completed   |   |
|      | Biyearly inspection and cleaning of outfalls               | Road Operations                    | Spring & Fall of every year, whenever<br>CVC issues flood watch/warning<br>(during/after ice jam and flood<br>events) | Recurring since November of 2022  | Recurring work underway   |   |
| 27   | Culvert and Sewer flushing                                 | Contract Services                  | Spring & Fall of every year & whenever conservation authorities issue flood watch/warning                             | Flushing completed in November 2023. Spring flushing to be scheduled.   | Recurring work underway   |   |
|      | Annual CCTV inspection of Sewers and<br>Culverts           | Contract Services                  | CCTV inspections to occur every spring  | Last inspection completed January 2023. New<br>inspection will be completed Spring of 2024 as per<br>annual spring inspection note (pending award of new<br>contract).  | Recurring work underway   |   |
| 29   | Increase frequency of mowing at outfalls                   | Parks                              | November 2022   | Increased mowing services at outfalls   | Recurring throughout the growing season every year, including four cuts each year               |   |
| 30   | Clear rock aprons at outfalls                              | Road Operations                    | November 2022   |   | Completed in November 2022.<br>Will recur twice yearly, Spring &<br>Fall, beginning Spring 2023 |   |
| 31   | Culvert at outfall #2 to be inspected<br>and assessed      | Engineering & Contract<br>Services | October 2022  | Visual and CCTV inspection completed. Minor repairs scheduled for Spring 2023.  | Repaired March 2023   |   |
| 32   | Review and asses the condition of floodwalls and berm      | Stormwater Management              |   | Geotechnical inspection and structural assessment of floodwalls and earth dykes. Final draft report to be   | In progress   |   |
| 33   | Commence Environmental Assessment<br>for flood remediation |                                    | Q2 2024   | Comprehensive look at flood risk and options to mitigate risk   | Planned   |   |
| 34   | Manhole inspection and bolting                             | Contract Services & Peel<br>Region | Q1 2023   | Inspection of all surface manhole lids (stormwater and<br>sanitary) to confirm they are bolted and not warped.<br>City confirmed all stormwater manholes are bolted<br>and not warped in January 2023. Region of Peel<br>confirmed sanitary manholes are bolted March 2023. | Completed   |   |

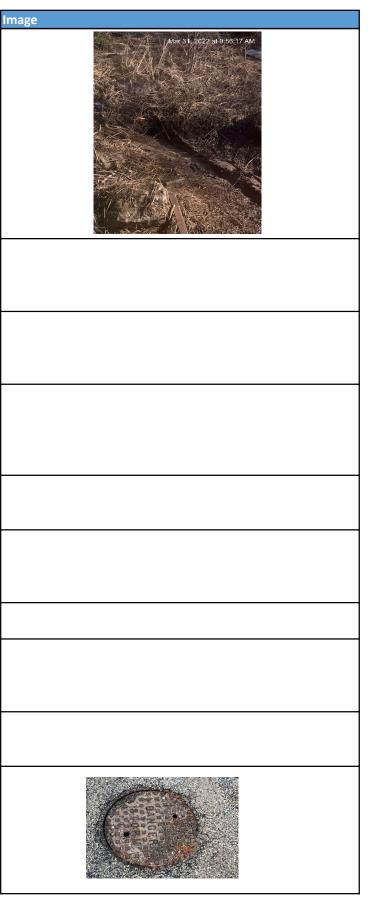

| Item | Work Required                          | Division Responsible | Estimated Start Date | Comments   | Status  | l |
|------|--|----------------------|----------------------|--|---------|---|
|      |  |                      |                      |  |         | Ι |
|      |  |                      |                      | Comprehensive inspection completed by consultant in  |         |   |
|      |  |                      |                      | 2023. Moving forward, recurring inspections will be  |         |   |
|      | Annual Structural Inspections of Flood |                      |                      | completed by Capital Works as part of recurring OSIM |         |   |
| 35   | Wall and Earth Dykes                   | Capital Works        | Fall 2024            | inspections of retaining walls.                      | Planned |   |

Image
